


ID	Task Mode	Task Name	Duration	Start	Finish	Aug '12			03 Sep '12			17 Sep '12			
						W	S	T	M	F	T	S	W	S	
1		SCAFFOLD	1 day	Mon 10/09/12	Mon 10/09/12										
2		8 PARKSIDE (E.W.I)	15 days	Tue 11/09/12	Mon 01/10/12										
3		8 PARKSIDE (INTERNALS)	20 days	Tue 11/09/12	Mon 08/10/12										
4		SCAFFOLD	1 day	Fri 21/09/12	Fri 21/09/12										
5		17 PARKSIDE	10 days	Mon 24/09/12	Fri 05/10/12										
6		150 ST CHADS RD	10 days	Mon 24/09/12	Fri 05/10/12										
7		131 ST CHADS RD	10 days	Mon 24/09/12	Fri 05/10/12										
8		SCAFFOLD	1 day	Fri 28/09/12	Fri 28/09/12										
9		15 LISTER RD	10 days	Mon 01/10/12	Fri 12/10/12										
10		11 LISTER RD	10 days	Mon 01/10/12	Fri 12/10/12										
11		13 LISTER RD	10 days	Mon 01/10/12	Fri 12/10/12										
12		SCAFFOLD	1 day	Fri 05/10/12	Fri 05/10/12										
13		107 ST CHADS RD	10 days	Mon 08/10/12	Fri 19/10/12										
14		50 RAPHAEL	10 days	Mon 08/10/12	Fri 19/10/12										
15		22 HANDEL CRESCENT	10 days	Mon 08/10/12	Fri 19/10/12										
16		SCAFFOLD	1 day	Fri 12/10/12	Fri 12/10/12										
17		8 MILTON GARDENS	10 days	Mon 15/10/12	Fri 26/10/12										
18		20 LONDON RD	10 days	Mon 15/10/12	Fri 26/10/12										
19		31 GAINSBOROUGH RD	10 days	Mon 15/10/12	Fri 26/10/12										
20		SCAFFOLD	1 day	Fri 19/10/12	Fri 19/10/12										
21		53 GAINSBOROUGH RD	10 days	Mon 22/10/12	Fri 02/11/12										
22		29 LYTTON	10 days	Mon 22/10/12	Fri 02/11/12										
23		49 LYTTON	10 days	Mon 22/10/12	Fri 02/11/12										
24		SCAFFOLD	1 day	Fri 26/10/12	Fri 26/10/12										
25		160 HATHAWAY	10 days	Mon 29/10/12	Fri 09/11/12										

Project: THURROCK CONTRACT W Date: Wed 19/09/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	Aug '12			03 Sep '12			17 Sep '12		
						W	S	T	M	F	T	S	W	S
26		86 HATHAWAY	10 days	Mon 29/10/12	Fri 09/11/12									
27		SCAFFOLD	1 day	Fri 02/11/12	Fri 02/11/12									
28		173 HATHAWAY	10 days	Mon 05/11/12	Fri 16/11/12									
29		4 THURLOE WALK	10 days	Mon 05/11/12	Fri 16/11/12									
30		26 THURLOW	10 days	Mon 05/11/12	Fri 16/11/12									
31		100 LENTHALL	10 days	Mon 05/11/12	Fri 16/11/12									
32		SCAFFOLD	1 day	Fri 09/11/12	Fri 09/11/12									
33		103 LENTHALL	10 days	Mon 12/11/12	Fri 23/11/12									
34		137 LENTHALL	10 days	Mon 12/11/12	Fri 23/11/12									
35		69 MILTON	10 days	Mon 12/11/12	Fri 23/11/12									
36		SCAFFOLD	1 day	Fri 16/11/12	Fri 16/11/12									
37		125 LENTHALL	10 days	Mon 19/11/12	Fri 30/11/12									
38		155 CROMWELL	10 days	Mon 19/11/12	Fri 30/11/12									
39		150 CROMWELL	10 days	Mon 19/11/12	Fri 30/11/12									
40		29 OAK ROAD	10 days	Mon 19/11/12	Fri 30/11/12									
41		SCAFFOLD	1 day	Fri 23/11/12	Fri 23/11/12									
42		21 HILLCREST	10 days	Mon 26/11/12	Fri 07/12/12									
43		60 SECOND	10 days	Mon 26/11/12	Fri 07/12/12									
44		58 SECOND	10 days	Mon 26/11/12	Fri 07/12/12									
45		69 HALL RD	10 days	Mon 26/11/12	Fri 07/12/12									




Project: THURROCK CONTRACT W Date: Wed 19/09/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

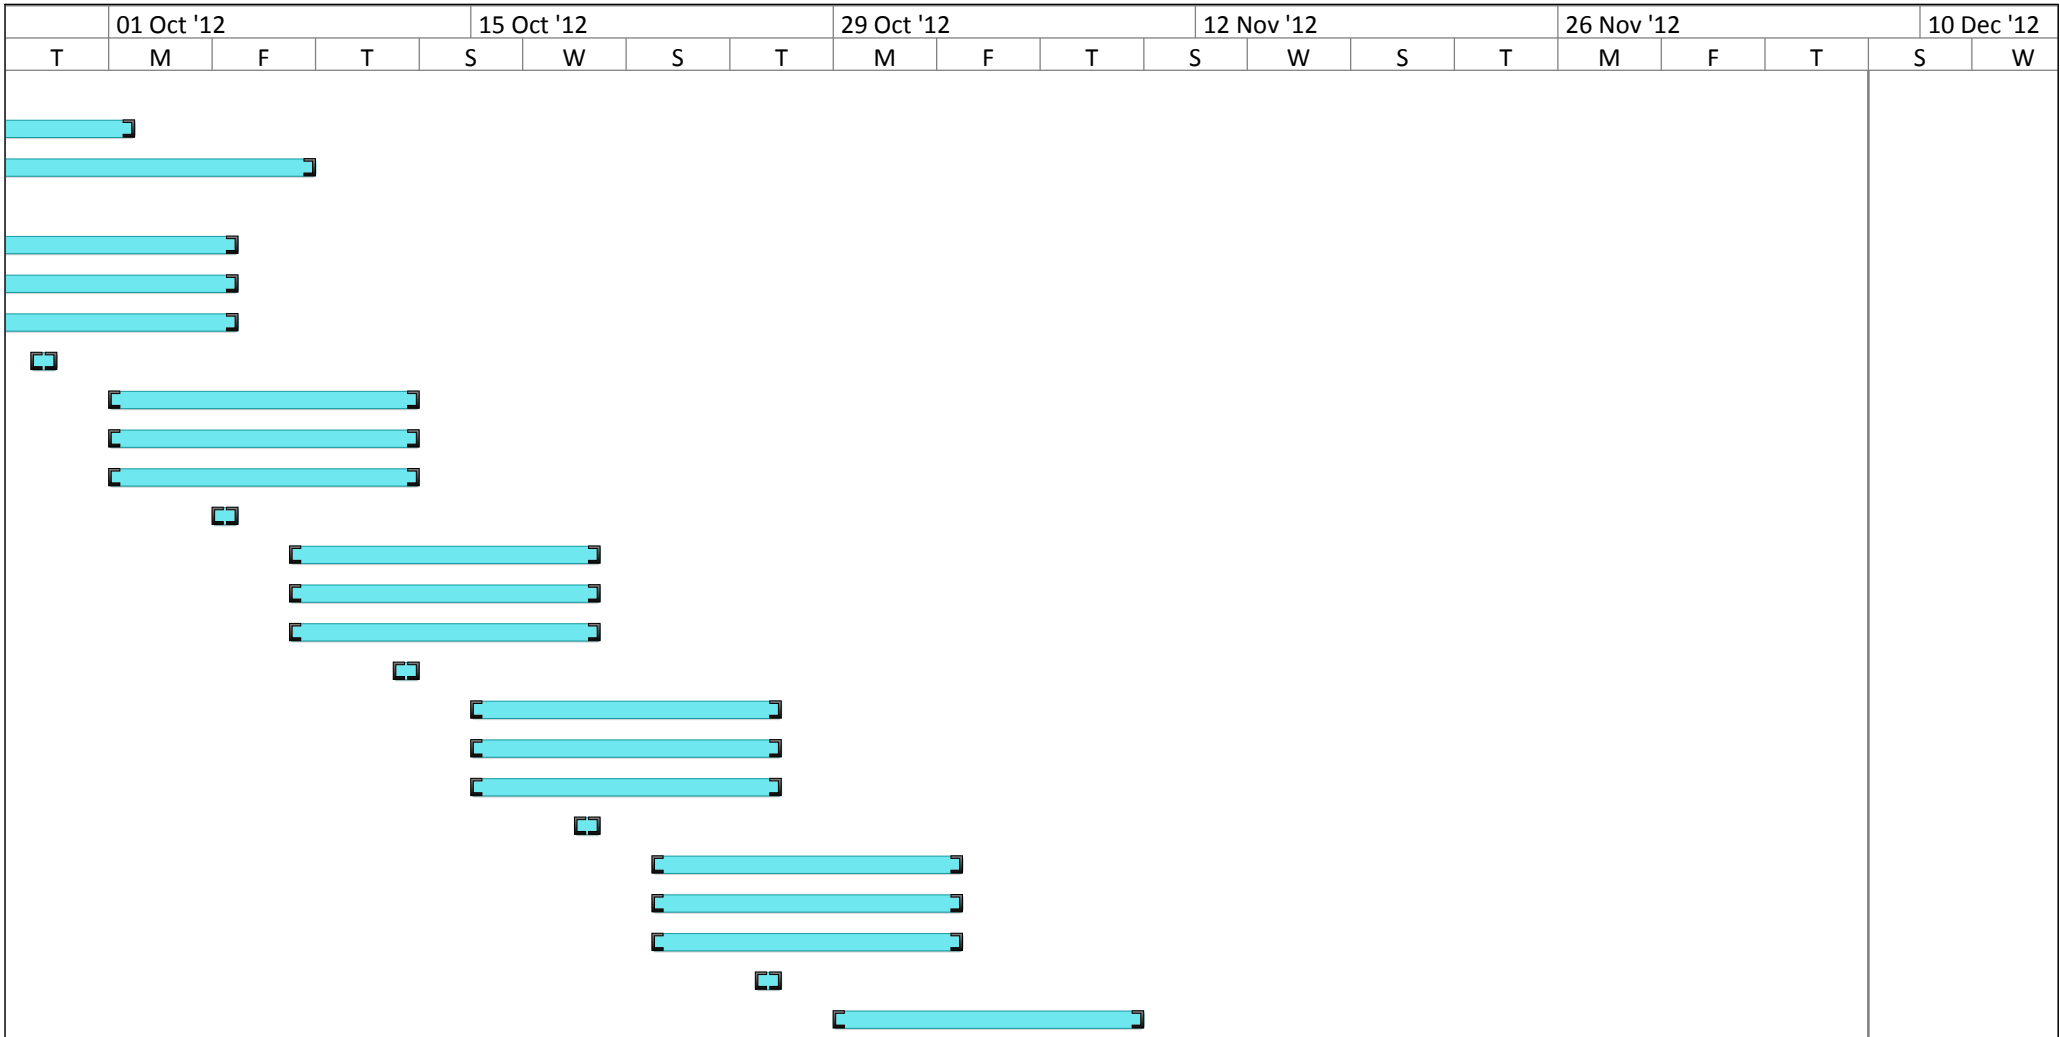

Project: THURROCK CONTRACT W
Date: Wed 19/09/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

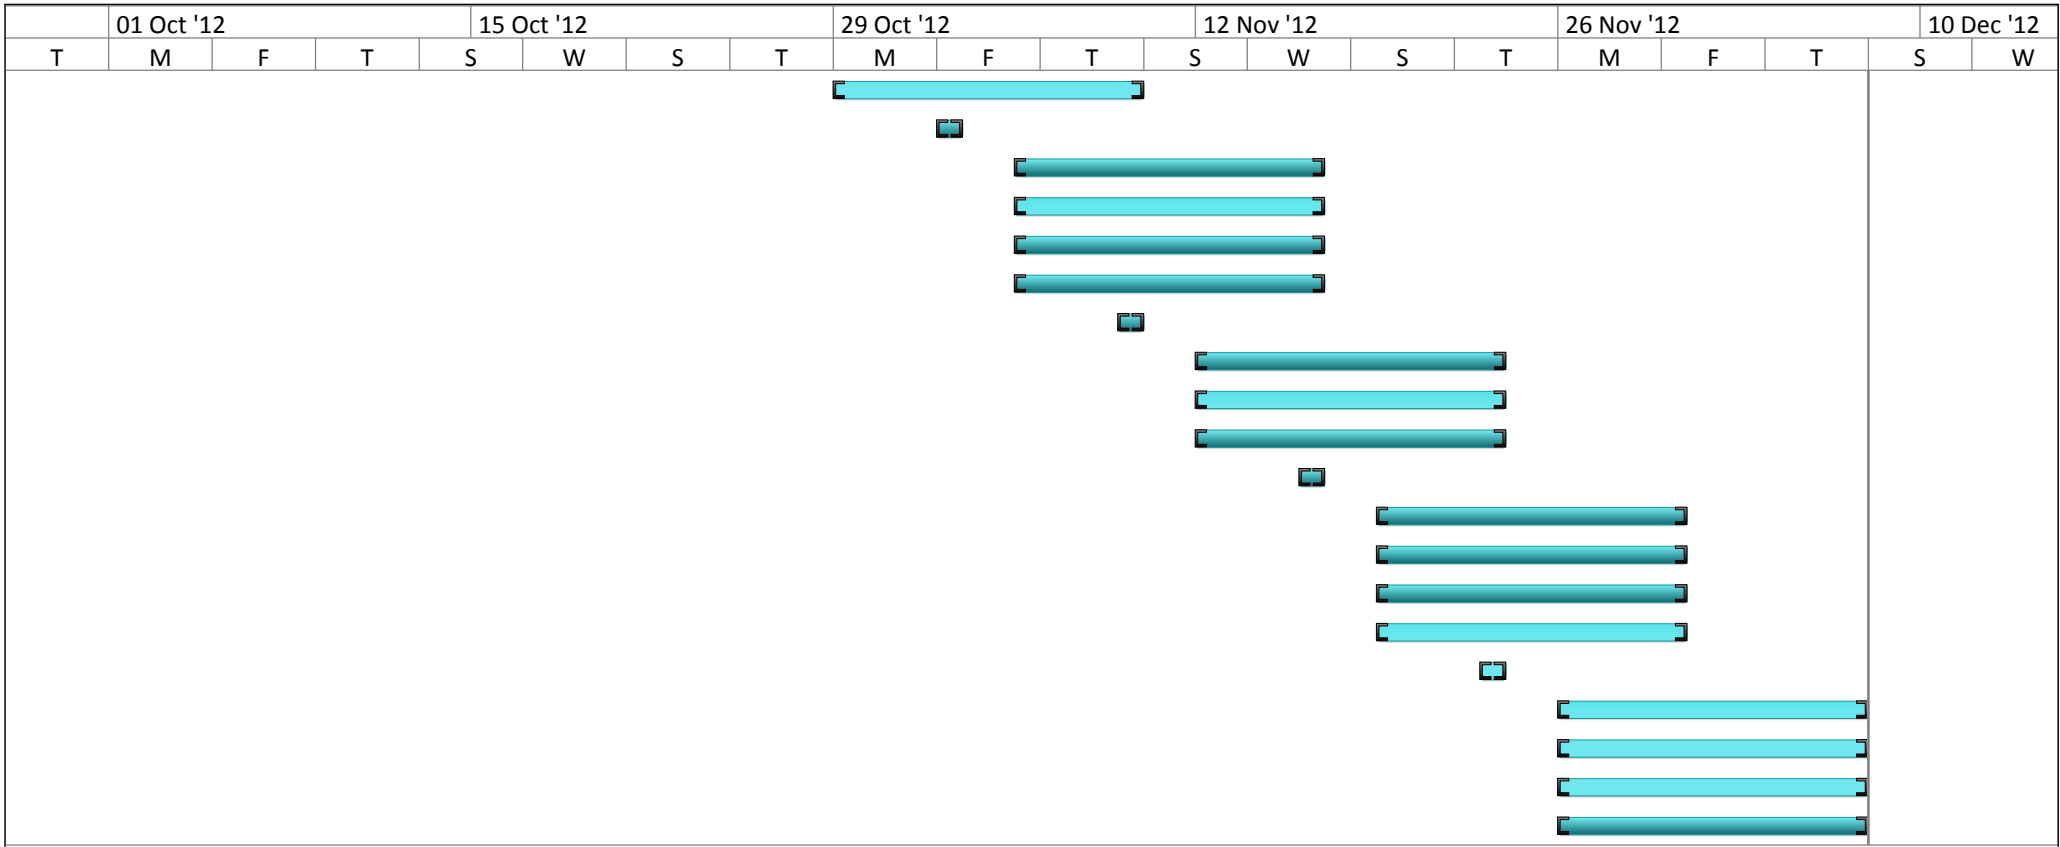



















Project: THURROCK CONTRACT W
Date: Wed 19/09/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	


Dec '12			24 Dec '12			07 Jan '13			21 Jan '13			04 Feb '13			18 Feb '13				
W	S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T

Project: THURROCK CONTRACT W
Date: Wed 19/09/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

Dec '12			24 Dec '12			07 Jan '13			21 Jan '13			04 Feb '13			18 Feb '13		
---------	--	--	------------	--	--	------------	--	--	------------	--	--	------------	--	--	------------	--	--

W	S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T
---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---



Project: THURROCK CONTRACT W
Date: Wed 19/09/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	
